Brigitta Noémi Bócz PMP®-certified Project Manager · International Projects & Agile Practice · Nantes

Agile-Vet: MVP planning, backlog design and a Daily Scrum simulation

How I scoped the first release of a clinic website, chose what to leave out, and, as Product Owner, identified two impediments and defined the next actions.

> **Simulated training project.** Produced individually and assessed in French for the Agile certification RS5487 (Simplon.co); certification obtained June 2026. Planned outcomes are marked as planned.

The problem

A veterinary clinic's website is outdated and unusable on a phone, with no online booking. Pet owners call for opening hours, the emergency number and prices, which ties up the front desk.

Three decisions

1. **Release scope.** Six of eight user stories, forming one complete journey: find information, book, get a confirmation. Early-slot alerts and self-service price editing were deferred because they are more complex to build and less important than the core journey for a first usable version.
2. **One Sprint Goal, not a feature list.** A first working, responsive site with the essential information and simple booking with confirmation, so every task could be checked against the goal.
3. **Impediments as product decisions.** At mid-sprint, the Daily Scrum surfaced an open question on the mobile menu (keeping the emergency number findable within seconds) and undefined booking rules. As Product Owner I took ownership of both and set the next actions: agree a simple menu with the number always visible, and clarify the booking rules with the clinic at once.

What I produced

- 8 user stories, checkable acceptance criteria
- Prioritisation by value, feasibility, MVP focus
- Sprint Goal; 5 tasks mapped to stories
- Trello board, work-in-progress limit of 2
- Daily Scrum, delivered live to the jury
- 17-page report, 14-slide deck (French)

Mid-sprint board, 18 April 2026

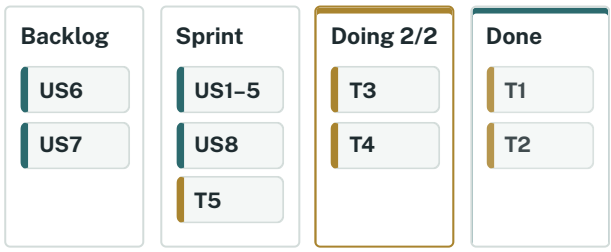

Teal edge: user story. Ochre edge: task.

What I would do differently

Slice stories vertically so each can be accepted on its own; agree content needs and open dependencies during refinement; and add one indicator per expected benefit, such as the share of appointments booked online.
